Windham Community Center

(months)

Period Highlight: 3

Plan Duration | Actual Start | % Complete | Actual (beyond plan) | % Complete (beyond plan
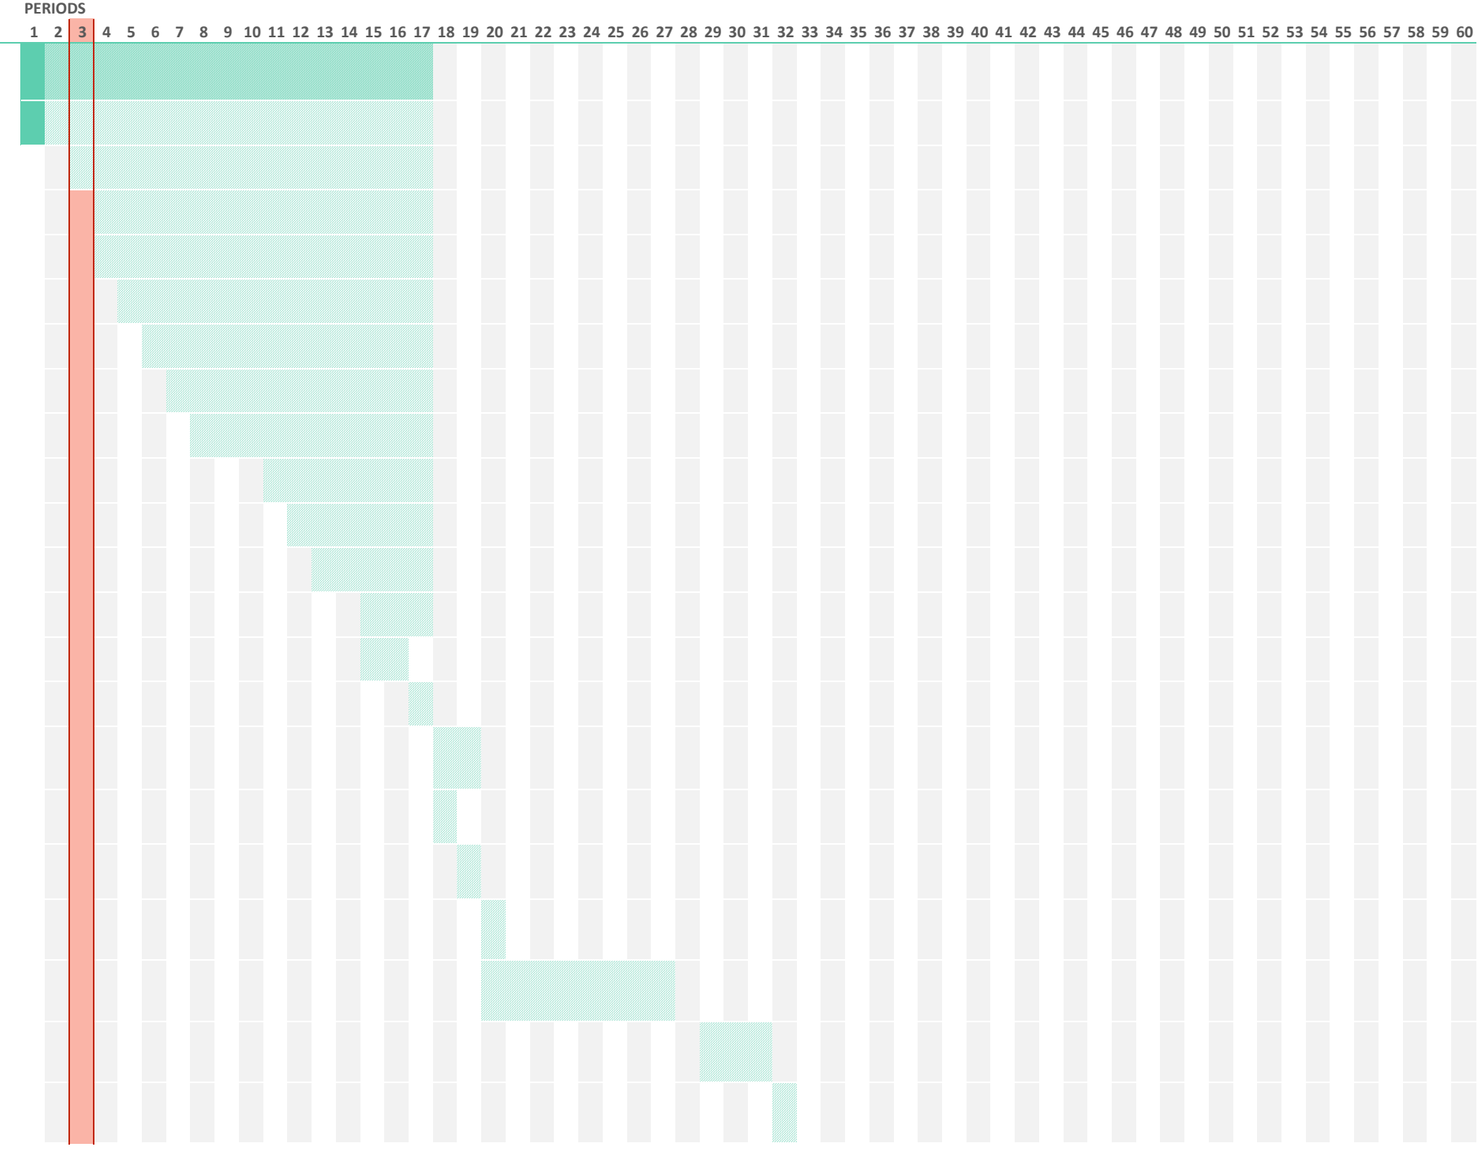
ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION	PERCENT COMPLETE
Pre-Construction & Planning	**1**	**17**	**1**	**17**	**7%**
Meeting November 25, 2024	1	17	1	1	**7%**
Meeting January 21, 2025	3	15		15	**0%**
Meeting February 1, 2025	4	14		14	**0%**
Meeting February 18, 2025	4	14		14	**0%**
Meeting March 18, 2025	5	13		13	**0%**
Meeting April 15, 2025	6	12		12	**0%**
Meeting May 20, 2025	7	11		11	**0%**
Meeting June 17, 2025	8	10		10	**0%**
Meeting September 16, 2025	11	7		7	**0%**
Meeting October 21, 2025	12	6		6	**0%**
Meeting November 18, 2025	13	5		5	**0%**
Meeting January 20, 2026	15	3		3	**0%**
Meeting February 17, 2026	15	2		2	**0%**
Meeting March 17, 2026	17	1		1	**0%**
Submission of Warrant Article for Town Meeting w/ Docs	18	2		2	**0%**
Meeting April 21, 2026	18	1		1	**0%**
Meeting May 19, 2026	19	1		1	**0%**
Windham Town Meeting Vote *(Town Meeting June 13, 2026)*	20	1		1	**0%**
Project Administration	20	8		8	**0%**
Permitting & Construction Documents (2026-2027)	29	3		3	**0%**
Construction Start (Q2 - 2027)	32	1		1	**0%**
